LAB 08 — INSTRUCTIONS

Manage Client Projects with Sub-tasks, Dependencies, Timeline and Linked Views


Topic 05 · Day 2 · Intermediate · Notion databases (timeline, sub-items, dependencies, linked views) · Alignment K3 · A3

Goal

You create the Projects and Tasks databases in Client Projects from the supplied CSVs, turn on sub-items and dependencies so date changes shift dependent tasks, plan the Nova Retail launch on a timeline, and embed linked views of the tasks inside each project page and on the Company Home dashboard.

What you will build

Projects and Tasks databases with sub-tasks, dependencies and a timeline, plus linked task views inside project pages and on Company Home

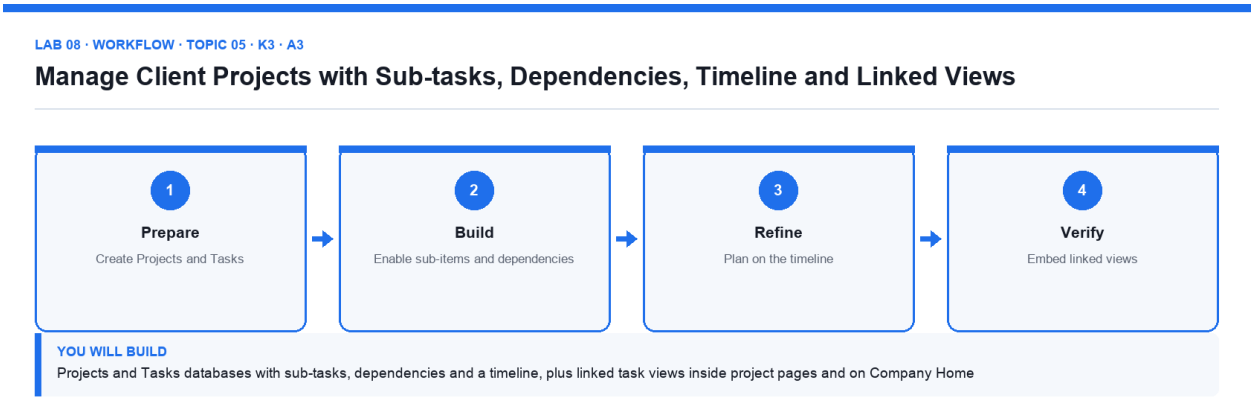

Files supplied in this folder

- projects.csv — Six client projects with client, dates, stage and budget
- tasks.csv — Twenty-four tasks with parents, dependencies, assignees and estimates

Detailed procedure

Step 1. Create the Tasks database

Open Client Projects. Import tasks.csv as a database named Tasks. Set Status → Status, Due → Date (with end date), Assignee → Person, Estimate (h) → Number, Priority → Select.

Step 2. Create the Projects database

Import projects.csv as Projects. Set Client → Select, Dates → Date range, Stage → Status, Budget (SGD) → Number with SGD format.

Step 3. Turn on sub-items

In Tasks click □ → Sub-items → Turn on. Notion adds Parent item and Sub-items properties. Using tasks.csv's Parent column, open each parent task and add its sub-tasks; the table shows a toggle arrow on parents.

Step 4. Turn on dependencies

Click □ → Dependencies → Turn on, choose Shift only when dates overlap, and set the Blocked by / Blocking properties. Using the Depends on column in the CSV, add each dependency.

Step 5. Add a timeline view

Add a Timeline view of Tasks, choose Timeline by Due, Month zoom, and Show table with Name, Assignee and Status. Dependency arrows appear between bars.

Step 6. Shift a date and watch dependencies move

Drag the 'Approve creative concept' bar two days later. The dependent 'Produce launch assets' task shifts too. Undo with Cmd/Ctrl+Z and note the behaviour in your README checklist.

Step 7. Group and filter the timeline

Group the timeline by Assignee, then filter Status is not Done. Add a table view named Overdue with filter Due is before Today AND Status is not Done.

Step 8. Embed a linked view inside a project page

Open the Nova Retail Launch project page. Type /linked view of database, choose Tasks, and Create new empty view. Filter it to Project contains Nova Retail Launch (create a Project relation property in Tasks first if it does not exist — Lab 9 completes this). Hide the database title.

Step 9. Add a dashboard linked view to Company Home

On Company Home add /linked view of database → Tasks → copy the Overdue view. Now the home page shows overdue work across all clients. Add a linked calendar of Content Calendar beside it in a second column.

Step 10. Lock views on the linked database

On the Company Home linked views use □ → Lock views so the dashboard layout stays fixed while data still changes.

Acceptance check

Tasks has parent tasks with sub-items and dependency arrows on the timeline, moving a blocking task shifts its dependents, the Overdue view lists only late open tasks, the Nova Retail Launch page shows only its own tasks in a linked view, and Company Home shows locked linked views of Tasks and Content Calendar.

Evidence to retain

Screenshot of the timeline with dependencies and of the Company Home dashboard.
